


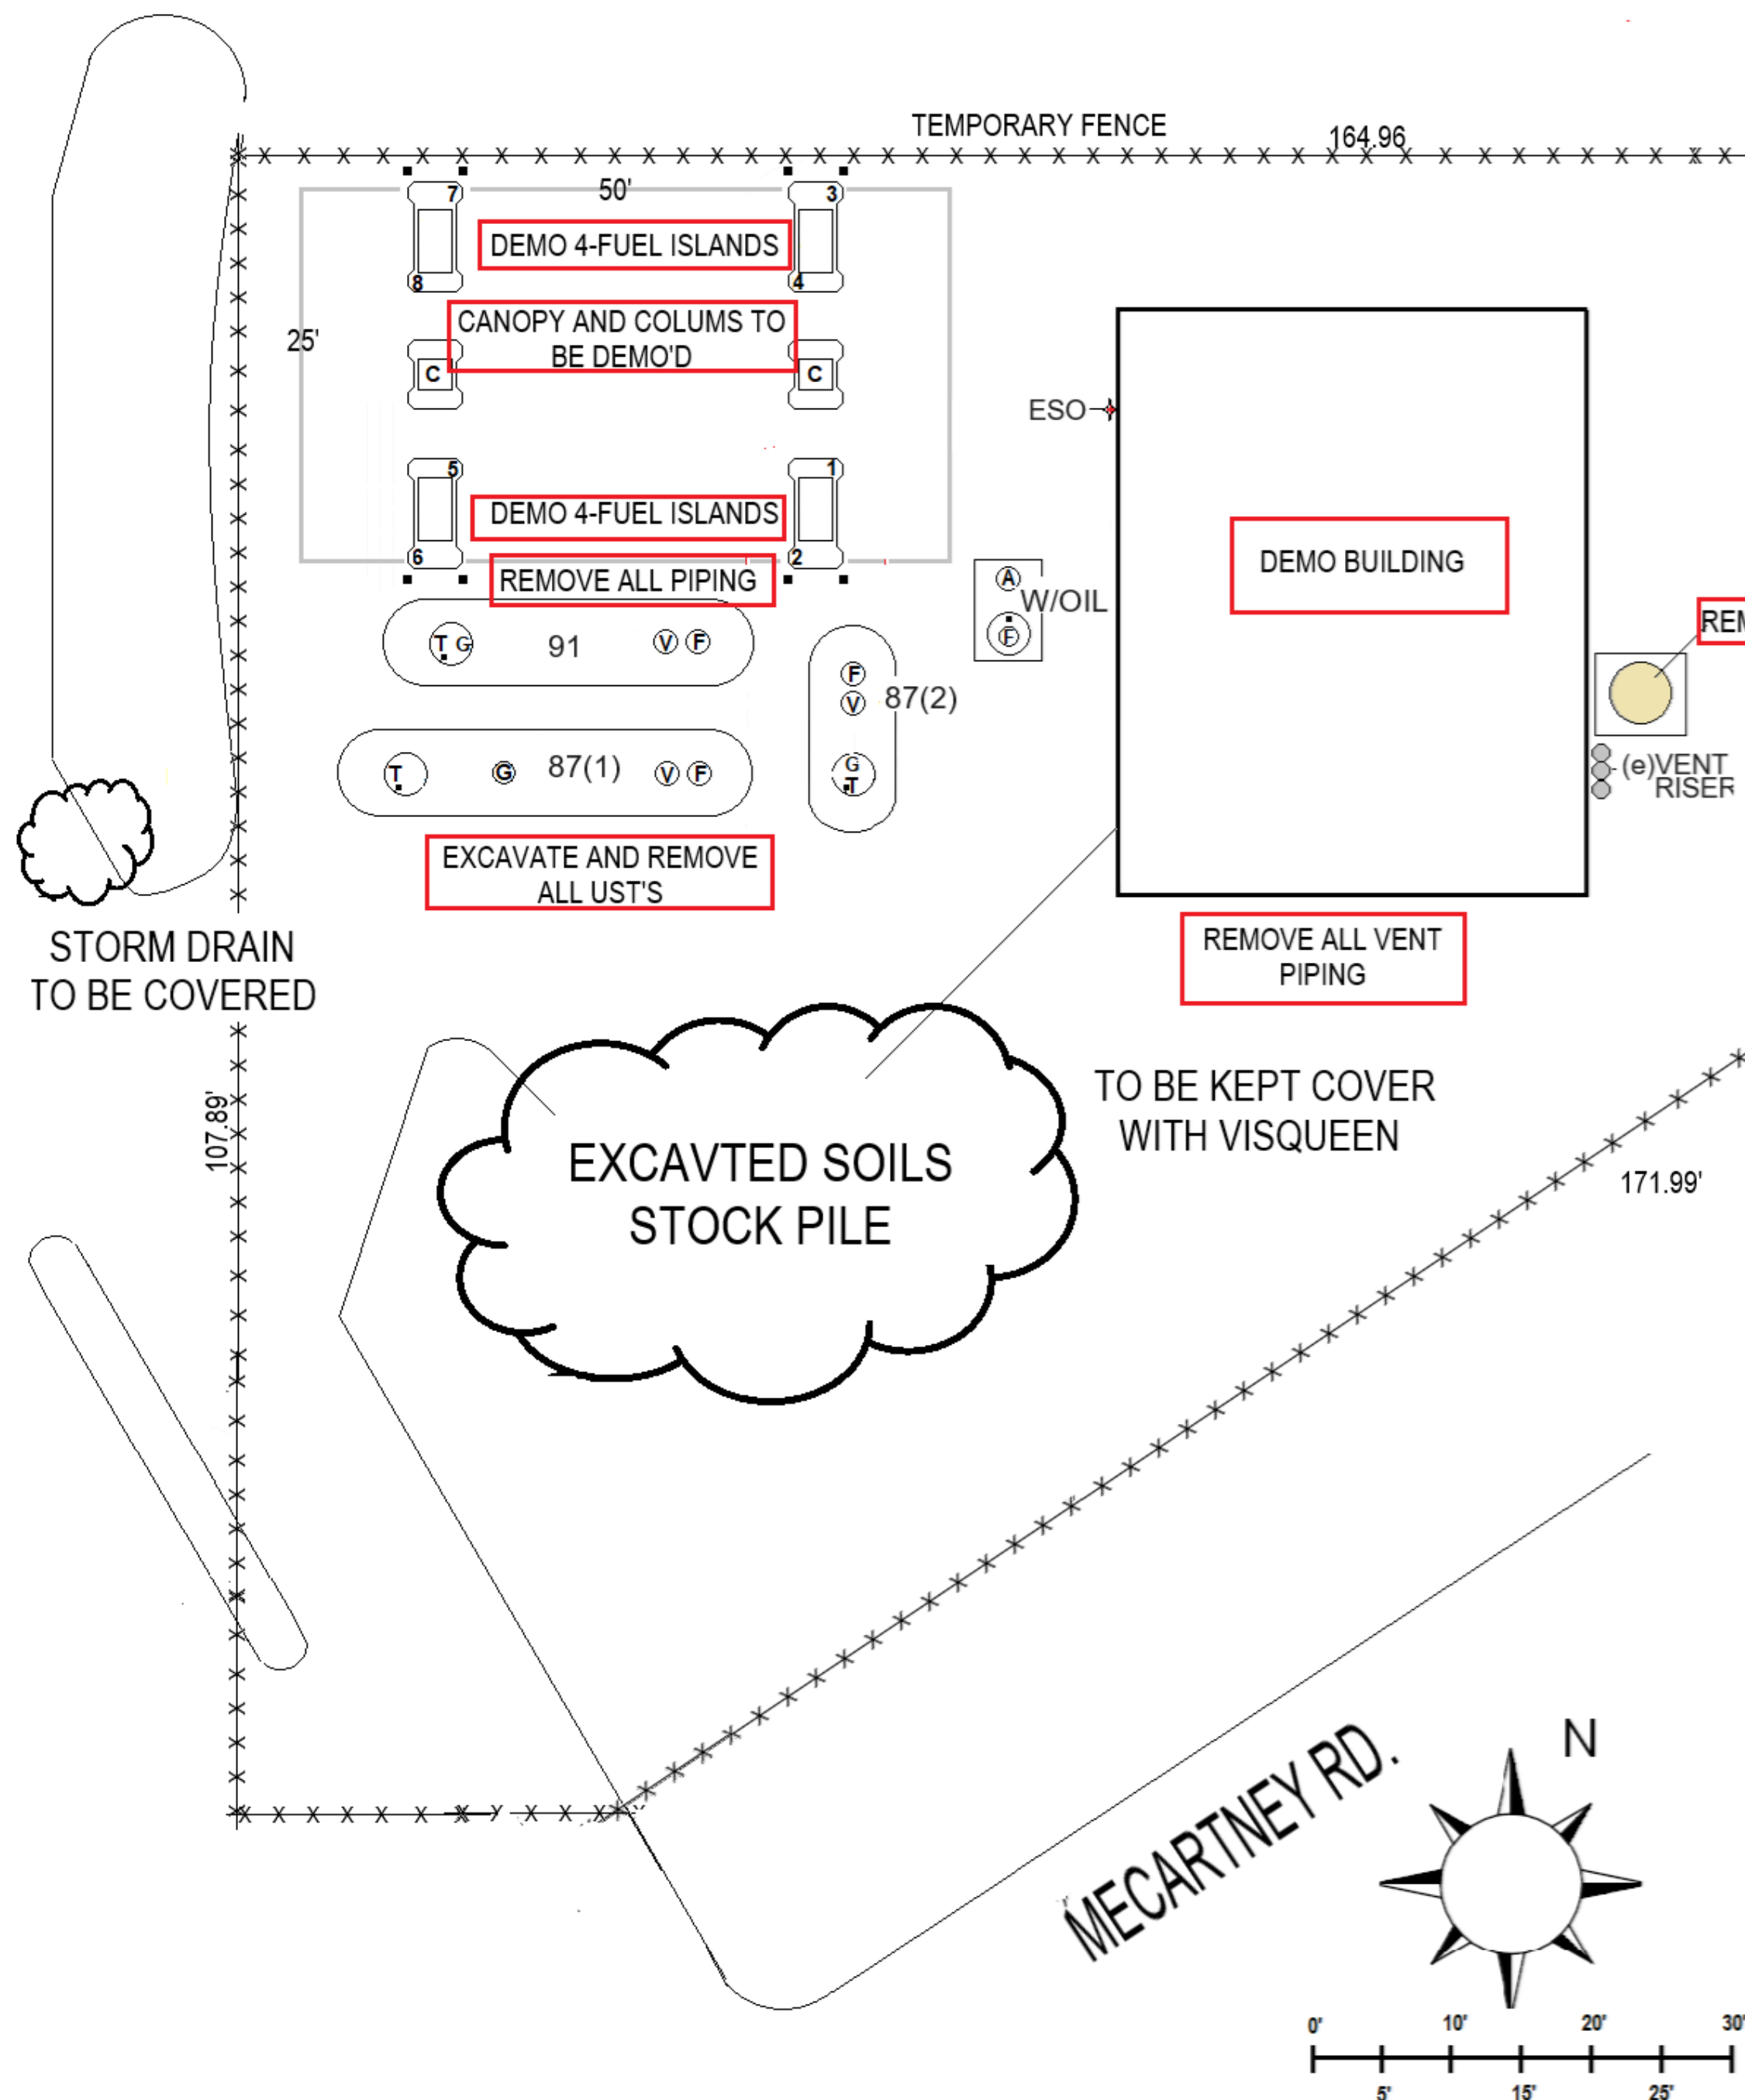

SCOPE OF WORK:

1. TASK #1 – PRE-TANK REMOVAL ACTIVITIES:
 - a. CGRS WILL SUBMIT PERMITS TO CUPA AND CITY OF ALAMEDA
 - b. NOTIFY PG&E & TELEPHONE/CABLE COMPANY OF SITE CLOSURE
 - c. MARK LOCATION OF UTILITIES
 - d. NOTIFICATION OF DIG ALERT BEFORE EXCAVATION
 - e. PREPARE SITE FOR UST REMOVAL AS REQUIRED
 - f. SCHEDULE DELIVERY OF TEMPORARY FENCING
 - g. SCHEDULE TANK CLEANING AND TANK DISPOSAL
 - h. SCHEDULE SOIL TEST SAMPLING
 - i. SCHEDULE LEAD AND ASBESTOS SURVEY
 - j. SCHEDULE BOTTOM CHECK (INSPECTION)
2. TASK #2 – REMOVE EXISTING UNDERGROUND STORAGE TANKS (UST'S)
 - a. DEMO CONCRETE, AND ASPHALT ABOVE THE TANK PIT
 - b. EXCAVATE THREE (3) FIBERGLASS UST'S (12K, 10K, & 6K) AND STOCKPILE SOIL ON SITE
 - c. EXCAVATE ONE (1) STEEL WASTE OIL TANK AND STOCKPILE SOIL ONSITE
 - d. DEMO CONCRETE OVER PIPING TRENCHES TO EXPOSE UNDERGROUND FUEL PIPING
 - e. DISPOSE OF DISPENSERS AND RELATED FUELING COMPONENTS
 - f. WASH FOUR (4) UST'S WITH RINSE LIQUID, AND DISPOSE OF RINSEATE BY PERMITTED HAULER TO PERMITTED RECYCLER/DUMPSITE (TOTAL VOLUME UP TO 700 GALLONS)
 - g. SOILS TESTING BY STATE CERTIFIED LABORATORY AS REQUIRED BY CUPA TO BE PERFORMED BY OTHERS
 - h. PROVIDE THE DISPOSAL OF FOUR (4) UST'S BY CERTIFIED HAULER TO PERMITTED RECYCLER AND PROVIDE CERTIFICATE OF DESTRUCTION
3. TASK #3 – BACKFILL TANK EXCAVATION
 - a. CALL FOR COMPACTION INSPECTIONS PRIOR TO BACKFILL
 - b. BACKFILL EXCAVATION WITH EXISTING STOCKPILED SOIL
 - c. IMPORT CLASS TWO BASE/GRAVEL TO FINISH BACKFILLING TO 4" BELOW GRADE
4. DEMO CANOPY & BUILDING
5. CONTACT COMPLETE SITE DEMO
6. CGRS WILL DEMO AND HAUL ALL BUILDING DEBRIS
7. CGRS WILL BACK FILL TO 4" BELOW FINISHED GRADE THE SITE AND PROVIDE COMPACTION REPORT
8. FINALIZE PROJECT
 - a. SUBMIT OWNER SUPPLIED CLOSURE REPORT TO CUPA
